Original/Duplicate/Triplicate

CONTRACT CERTIFICATE

Date.....2020

No: First and Final Bill (For Other Works)

Division: **Project** Sub-Division: **Project**

Bill Received No. Dated Divisional / Sub Divisional Cash Book Voucher No..... Dated.....

Work Code: 004-20-000006

Schedule Docket No. Head of Account: P-3692 Est.Cost- **100.00 Lakhs**

Name of Work: **Development of Parks and construction of Toilets at A Sector Parks in Ward No 04 Yalahanka New Town**

Name of Contractor and Full Address: **Sri. K Gopireddy**

Reference to Agreement No: **03/2020-21** Date: **16/04/2020**

Certified that the measurements were taken by me on 5/03/2021 and recorded of Pages 583501-26 of measurement Book No. 11/2000-21 and that the work is satisfactorily executed.

Officer in charge of work

Contractor

Certified that the measurement were taken by me on 05/03/2021 and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of and imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Sub-Division Officer

II Memorandum of Payment

1) Total value of work done or supplies made as per account within
2) Deduct amount to be held in reserve being .....percent Rs.....
3) " Balance
4) Deduct Payment:
   a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D. No..... towards cash advance recovery of
   b) Payments Now made } cost store or other material supplied. / recovery of amount creditable to this/other work / Amount paid on this bill Cheque / Cash.
5) Balance being unpaid value of work done held in reserve.
6) Deduct cash advance made on the Office cash Book Voucher No..... dated.....less adjustments.
7) Net amount due to or from Contractor
8) Advance to Contractor for materials brought to site (as detailed) within.
9) Value of Government materials supplied.

Amount adjusted

GROSS BILLRS 1,00,49,065/-
Addl GST 1% 1,00,491/-
CESS 1% 1,00,491/-
CBFO 1% 1,00,491/-
Royalty 62,058/-
CWST 83,724/-
SWST 83,724/-
TDS Deducting 4,52,536/-
Net Payables 95,96,529/-

unadjustments items.

Total amount adjusted -

Contractor's Signature

Received Rs..... (in words).....
.....
by cash and by adjustment of Payment as per memorandum
(in final settlement of all demands)

(For use in the Office)

Witness
1.
2.

Stamp

Audited & Admitted for Rs.....
Rs. 1,00,49,065/-
.....
Rs. 95,96,529/-
by Cheque
and Rs. 4,52,536/-

Dated Signature of Contractor

Paid by me by Cheque No.....Dated.....
Cash Rs.....
Dated.....
Initials of Officer making payment

Executive Engineer

Acctt. Supdt.
Project Division
B.B.M.P.

Exe. Engineer
Project Division
B.B.M.P.

Scanned by TapScanner

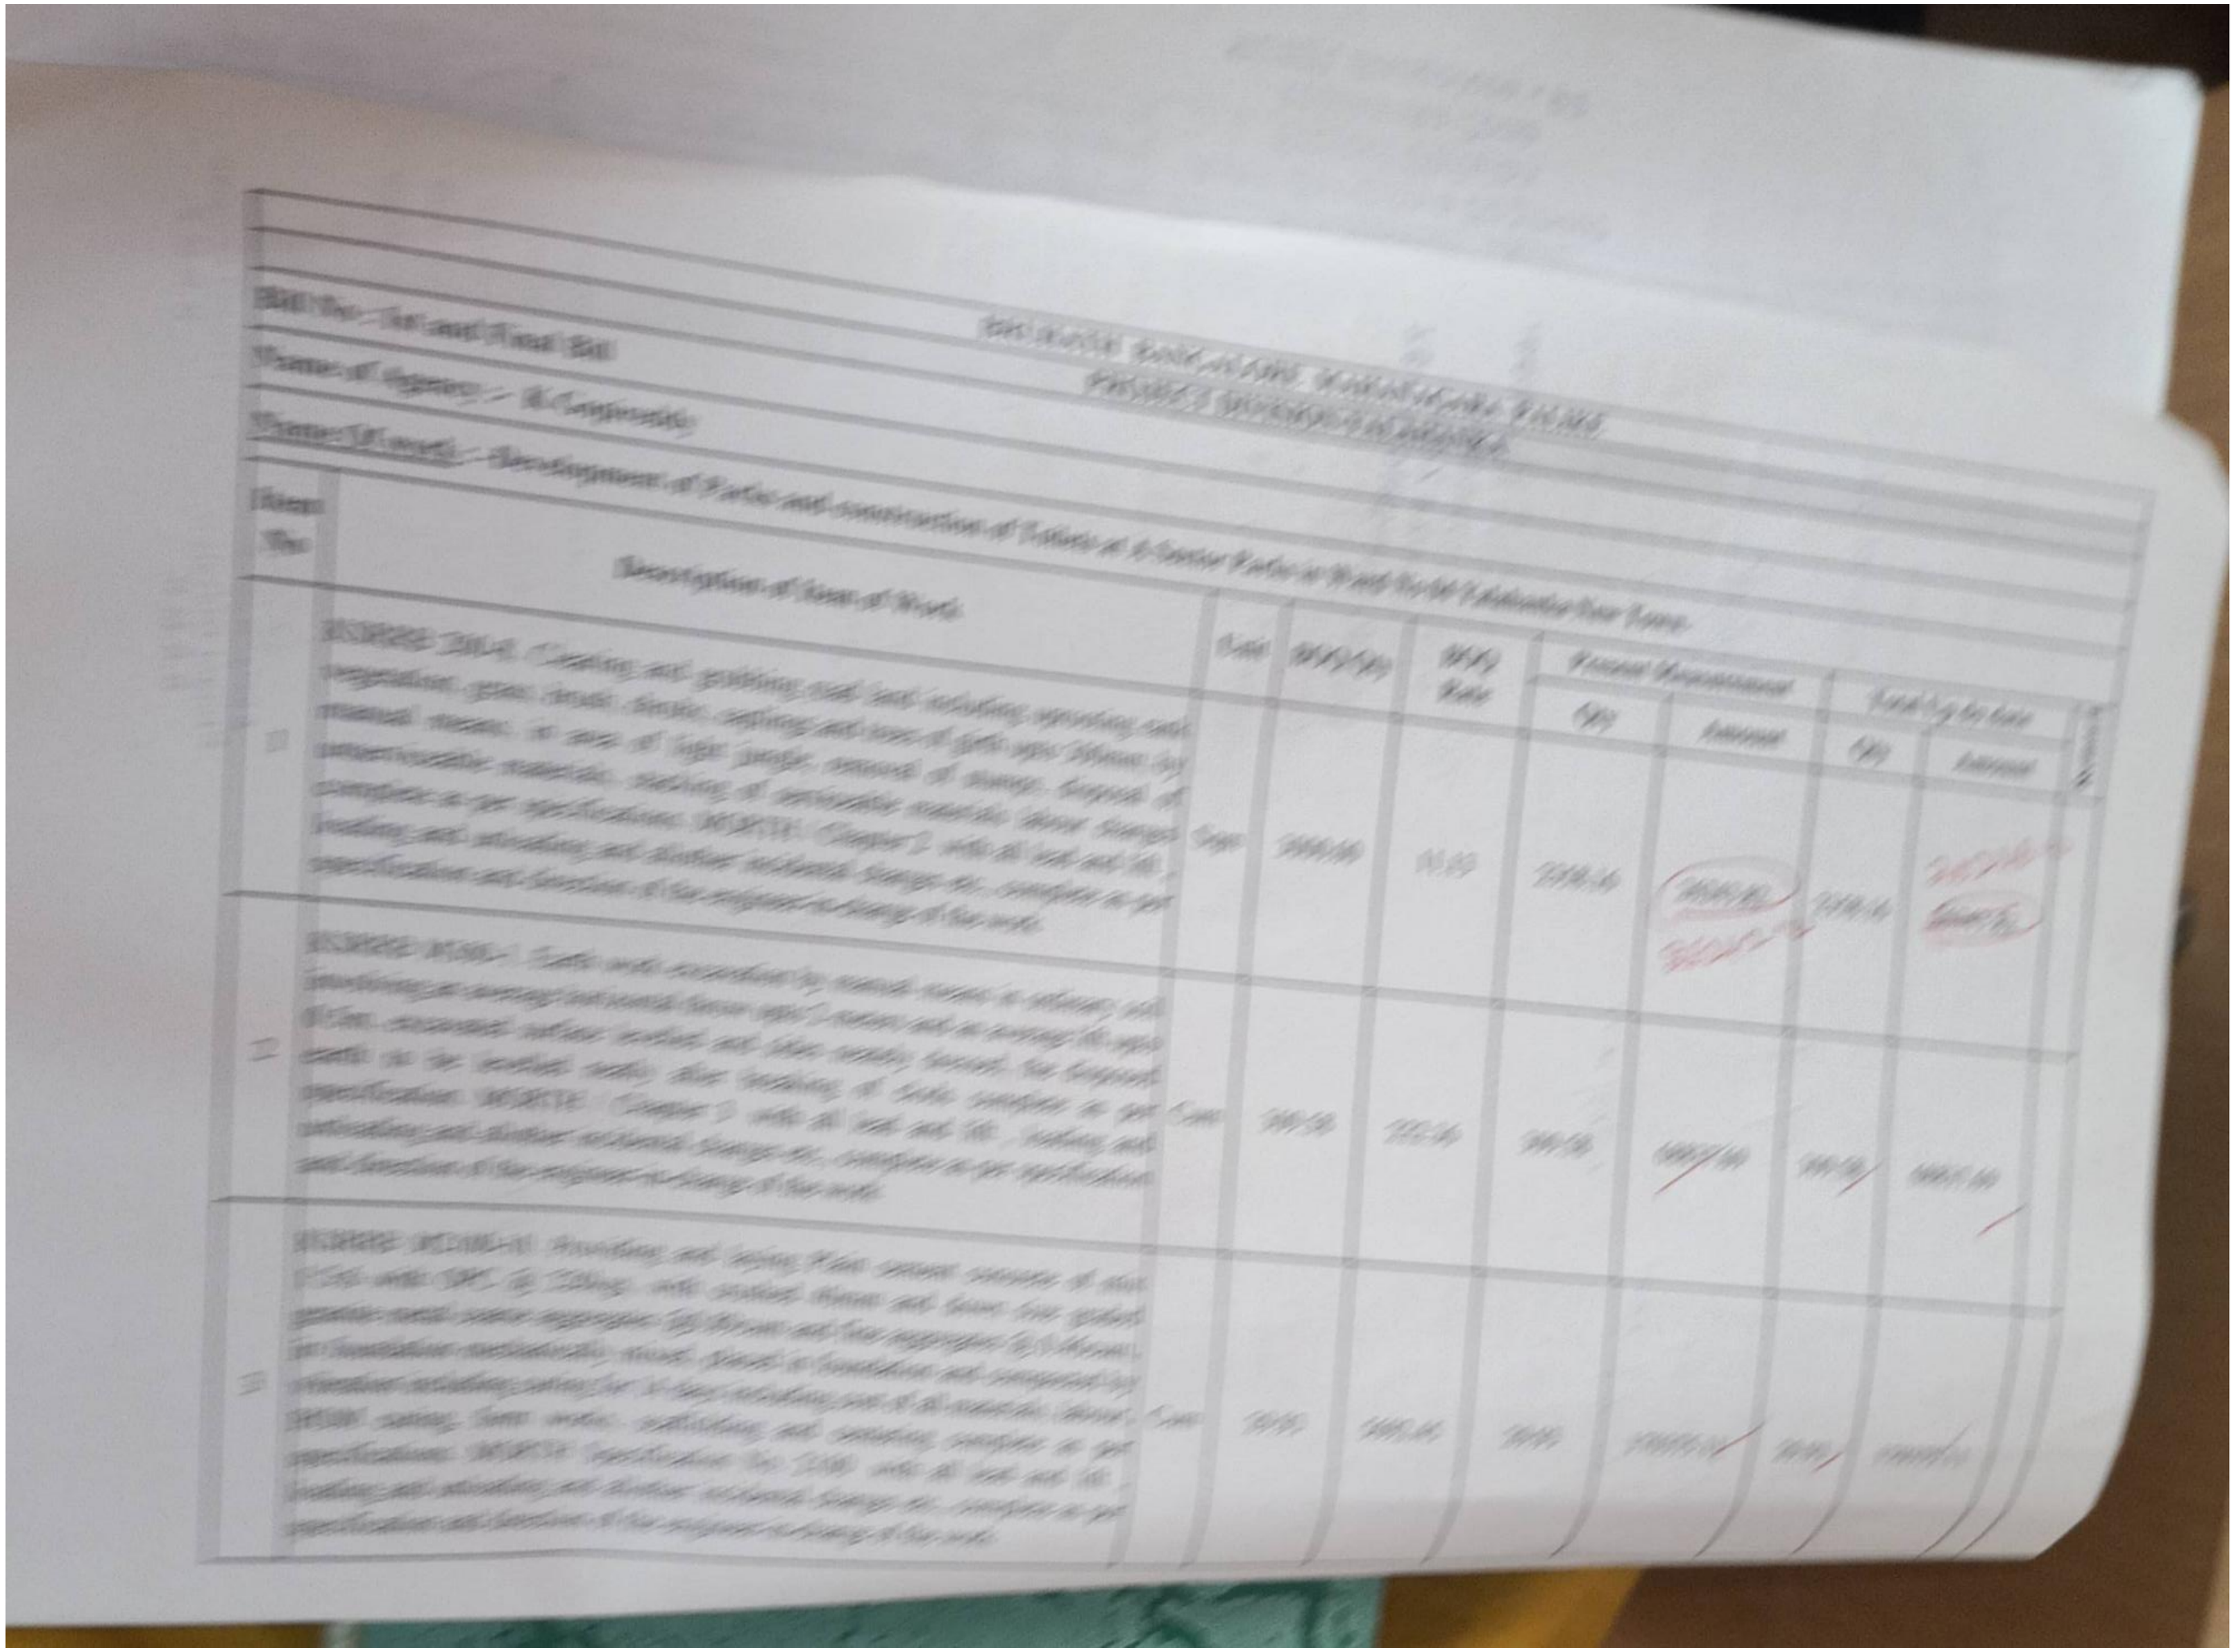

Scanned by TapScanner

4	KSRB 5.4-3 : Providing and constructing granite / trap / basalt size stone masonry in superstructure with cement mortar 1:6 , edges of stones chistle dressed in courses not less than 15 cms high, bond stones at two m. apart in each course including cost of materials, labour, scaffolding, curing complete as per specifications. KBS 5.1.13 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	116.52	5841.58	116.52	680660.97	116.52	680660.97	
5	KSRB 15.1.3 – do – Providing ruled pointing to coursed stone masonry with cement mortar 1:3, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	212.86	111.12	212.86	23653.30	212.86	23653.30	
6	KSRRB M2200-5.9. Providing and laying Design mix M20 with OPC @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.46cum, with superplastisiser @3lts confirming to IS9103-1999 Reaffirmed-2008 including cost of materials, labour, HOM curing, form works, scaffolding and centering complete as per specifications. - i) Upto 5 m height. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	8.45	5757.00	8.45	48646.66	8.45	48646.66	
7	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregtes @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, ncluding cost of all materials, labour, HOM of machinery, curing complete as per specifications. Specification No. KBS 4.1, 4.2. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	18.38	6169.51	18.38	113395.53	18.38	113395.53	

Scanned by TapScanner

8	Providing and fixing for flooring 20mm thick gang saw water cut sadarhalli gray granite in CM 1:4 proportion, cut to required shape, pattern with paper joints, finished with cement mortar using white cement and colour pigments to match the colour of slab making through jointing with sealant, groves in joints including cost of curing - minimum width of 900mm. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	79.95	2202.42	79.95	176083.26	79.95	176083.26
9	KSRRB M400-19: Construction of Median and island above road level with approved material deposited from borrowpits, spread, sloped and compacted as per Clause 400.7 complete as per specifications. MORTH Specification No.407 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	cum	320.18	232.59	320.18	74472.22	320.18	74472.22
10	KSRRB M400-17: Providing, laying, spreading and compacting graded stones aggregate to Wet Mix Macadam specifications including pre mixing the material with water at OMC in mechanical mix plant carriage of mix method of tipper to site,Laying in uniform layers with paver in subbase/base course on the well prepared surface and compacting with vibratory rollers to achive the desired density complete as per MORTH specification No. 406.etc with all lead and lifts and as per directions of the Engineer-in-charge with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	cum	8.45	2101.14	8.45	17754.67	8.45	17754.67
11	Providing and laying/fixing cement base, precast, pre polished cement concrete, designer tiles 25mm thick for flooring conforming to IS 1237 heavy duty tiles for flooring, treads of steps and landing, laid on a bed of 12mm thick cement mortar 1:3 mis finished with flush pointing using white cement, including cost of materials, including cutting, griding the edge to half/full round wherever required, labour, curing complete as per specification. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work (Avaliable Cobble stones)	Sqm	42.25	1371.09	31.91	43751.34	31.91	43751.34

Scanned by TapScanner

12	KSRB 14.6-1: Providing & laying heavy duty cobble stones 60mm thick interlock pavers,using cement & course sand for manufacture of blocks of approved size ,shape and colour with a minimum compressive strength of 281 kg per sqm over 50mm thick sand bed (Avg thickness) and compacting with plate vibrator having 3 tons compaction force thereby forcing part of sand underneath to come up in between joints, final compaction of paver surface joints into its final level, including cost of materials, labour and HOM of machineries complete as per specifications. Specification No. KBS with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	992.50	1171.88	992.50	1163088.30	992.50	1163088.30
13	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114 and 165 mm respectively, 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting, including form work, curing, including cost of all materials, labour, hire charges of machinery, loading, unloading, lead and lift, transportation etc., complete. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	No's	882.00	454.06	882.00	400481.58	882.00	400481.58
14	KSRRB 800-1. Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications. MORTH Chapter 8 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	138.95	89.03	138.95	12370.93	138.95	12370.93
15	Providing chain link fencing 50mm size of 8 guage properly stretched between existing rectangular poles and fixed with suitable bolts & nuts, the free ends shall be welded to the pole and block pipe at top and bottom as required including cost of all materials, labour, lead and lifts and as per the directions of the Engineer-in-charge of work including two coats of approved quality paint over one coat of shop paint with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	420.00	795.72	420.00	334202.07	420.00	334202.07

Scanned by TapScanner

16	Supplying and fixing M.S. Rectangular poles made out of 2 equal angles of 65x65x6 mm welded together and fixed in CC (1:2:4) WITH 2 NOS 16mm dia M.S. hold fast rods each of length 25 cms. Including cost of all materials cutting, bending scaffolding wherever necessary, nicely finishing the welded joints with all lead lifts and as per the directions of the Engineerin - charge of the work and including providing 2 coats of approved quality paint over one coat of shop painting (excluding cost of earthwork and concrete) with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	m	160.80	955.98	160.80	153720.93	160.80	153720.93	
17	Providing and fixing M.S. Block pipe of 38mm dia, of heavy guage of 14 including removing the bends, cutting the pipe, and fixing pipe in between the existing two verticle poles (M.S. rectangular poles) and spot welding the chain link with M.S. block pipe including cost of all materials wastage in cutting, and scaffolding wherever necessary with all lead and lift as directed by the Engineer-in-charge of work etc., complete including two coats of approved quality paint over one coat of shop paint. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	m	130.00	454.06	130.00	59027.90	130.00	59027.90

Scanned by TapScanner

18	Fabricating, providing and erecting in position Hot dip galvanized Gate. Using 72 x 72 x 4.8mm Sq. G I Pipe Frame with top pipe bending in heavy duty hydraulic press with sand packing and hot bending to form double arch as per drawing profile, 20mm hot dip galvanized sq. rod for verticals at 150mm c/c, as shown in the drawing including providing hot do galvanized forged ornamental design in between rods and heads at top, middle and bottom. Intermediate supports of 75x12mm and 50X6mm arch bent to hot dip galvanized flats. the work is inclusive of throughing GI, flat GI Sqm. rods, placing, welding all the joints including grinding, finishing metal patty, painting two coats enamel painting. The rate is inclusive of all materials Like G I Sq. GI Pipe, GI Forged designs etc., heavy duty hinges are made out of 75mm sold sq. block assembled with 20mm du bearing in three places for each flop. Heavy duty locking arrangement of low places including cost of labour, painting, erection charges using hoist pulley cranes with all lead and lift, loading, transportation, unloading, scaffolding charges and all other incidental charges for successful completion of the work as per directions of the Engineering charge of the work	Sqm	10.50	13097.53	10.50	137524.11	10.50	137524.11	
19	Fabricating, supplying & erecting M.S. angular Truss for all spans as approved design and drawing. The entire truss is anchored suitably by using 4 Nos. of M.S. anchor bolts at each support, with base plate and shoe plate.The work includes cutting, straightening, placing in position of M.S angle and wleding wherever necessary, and applying one coat of red oxide primer coat to all the members including cost of all materials, labour charges, & hire charges of machineries for cutting, welding, grinding & erection equipments, etc., complete as per specification. (Page No. 43 Item No. 7.30 of CSR 2018-19).	kg	2045.10	142.45	2045.10	291325.38	2045.10	291325.38	
20	KSRB 8.4-1 : Providing and fixing Mangalore tile roofing using first class tiles with necessary special tiles for ridges and hips, teak wood reepers of size 50x25mm and pointed with cement mortar 1:4 over the existing rafters including cost of materials, labour, curing complete as per specifications. Specification No. KBS 8.17. (P.No. 49, I.No. 8.10 of PWD SR 2018-19)	Sqm	49.00	1188.57	49.00	58239.97	49.00	58239.97	

Scanned by TapScanner

21	KSRB 15-18.2 : Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of materials, labour, complate as per specifications.(P 120/ I.15.74 PW,P & IWTD SR - 2018-19)	Sqm	478.28	105.72	478.28	50565.59	478.28	50565.59 50563.0	
22	KSRB 2-2.1 : Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. specification. No. KBS 2.1(a) / 2.3.5 (Page no -5, item no - 2.3)	Cum	96.96	339.03	96.96	32871.01	96.96	32871.01	
23	KSRB 2-2.1 : Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. specification. No. KBS 2.1(a) / 2.3.5 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	79.16	339.03	79.16	26836.21	79.16	26836.21	
24	KSRB 2-2.1 : Earthwork excavation for foundation of buildings, water supply, sanitary lines and electrical conduits either in pits or in trenches 1.5m and above in width, in ordinary soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. after breaking of clods complete as per specifications. specification. No. KBS 2.1(a) / 2.3.5 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	45.49	339.03	44.41	15055.13	44.41	15055.13	

Scanned by TapScanner

25	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @220kgs, with 40mm and down size graded granite metal coarse aggregates @ 0.892cum and fine aggregates @ 465 cum machine mixed, machine mixed,concrete laid in layers not exceeding 15 cms, thick well compacted, in foundation and plinth, including cost of all material, labour HOM Machinery curing complete as per specification, with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	13.26	5889.44	13.26	78067.41	13.26	78067.41 7893.0	
26	KSRB 4-6.1 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per specificaitons. Specification No. KBS 4.6.2 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	31.42	292.54	31.42	9191.74	31.42	9191.74	
27	KSRB 4-6.4 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached pilasters, buttresses, plinth cills and string courses cost of all materials, labour complete as per specifications. Specification No. KBS 4.6. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	221.40	405.93	187.01	75913.59	187.01	75913.59 75912.0	
28	KSRB 4-6.5 : Providing and removing centering, shuttering, strutting, propping etc., for columns, pillars, post and struts, square / rectangular/ polygon in plan including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	45.76	517.05	45.76	23660.43	45.76	23660.43	
29	KSRB 4-6.2 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for suspended floors, landings, balconies and likes, thickness upto 200 mm including cost of all materials, labour complete as per specificaitonsupto 3.50m from ground level. Specification No. KBS 4.6. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	116.20	453.56	116.20	52703.30	116.20	52703.30	

Scanned by TapScanner

30	KSRB 4-6.7 :Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for sides and soffits of beams, beam haunchings, cantilever girders, bressumers and lintels not exceeding 1m in depth including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	88.35	331.10	88.35	29252.37	88.35	29252.37	
31	KSRB 4-6.10 :Providing and removing centering, shuttering, strutting, propping etc., for chajjas, corbels etc., including edges including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	5.04	366.25	5.04	1845.89	5.04	1845.89	
32	KSRB 4.2.2 : Providing and laying in position reinforced cement concrete of Design mix M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregtes @ 0.460 cum, with super plasticisers @ 3 liters confirming to is 9103-1999 reafirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation for footings, pedastals, retaining walls, return walls, walls (any thickness) including attached pilasters, columnspillars, posts, struts, buttresses, bed blocks, anchor blocks & plinths etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1, 4.6 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	47.15	6416.69	47.11	302299.32	47.11	302299.32	

Scanned by TapScanner

33	KSRB 4.2.8: Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.46cum, with superplastisiser @3lts confirming to IS9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in ground floor level for roof slabs, staircase, lintles, and beams retaining walls, return walls, walls (any thickness) including attached plasters, columns, pillars, posts, struts, buttresses, string or lacing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1, 4.6. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	26.46	6680.89	26.46	176788.42	26.46	176788.42	
34	KSRB 4.2.10 : Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 24kgs, with 12mm and down size graded granite metal coarse aggregates @0.05175cum and fine aggregtes @ 0.0345cum, with superplastisiser @0.225lts, machine mixed, well compacted for plain chajja of 7.5 cms. average thickness, upto ground floor level, including cost of all materials, labour, HOM of machinery, finishing, curing, complete but excluding cost of reinforcement as per specifications. Specification No. KBS 4.1, 4.6 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	5.04	498.91	5.04	2514.52	5.04	2514.52	
35	KSRB 4.9.2 : Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost of materials, labour, HOM of machinery complete as per specifications. Specification No. KBS 4.6.3 - TMT bars Fe 500 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	MT	9.82	80467.78	9.82	790370.63	9.82	790370.63	

Scanned by TapScanner

36	Waterproofing of RCC Terrace / podium slab / toilet / utilities / water retaining structure by preparing the surface by chipping and cleaning and Grouting of Honey comb, voids,cracks / construction joints with cement slurry (1kg cement added in 10 ltr of water) added with 100gm of inorganic accelerator, followed by spraying of liquid biological modified alkaline earth silicates @ 0.40 ltr per sqm on whole surface to reduce the micro porosity and allowing it to dry, curing the surface for the silicates to penetrate deeper into the concrete and spraying waterproofing impregnate liquid containing silane and silanol linear copolymer @ 0.50 ltr per sqm and finally applying polymer slurry made out of cross linked acrylic / styrene / butadiene & cement in the ratio of 1:0.1, @0.50kg/sqm on the whole surface, including all labour charges tools and equipments, all complete as per the specification with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	130.00	596.43	130.00	77535.53	130.00	77535.53
37	KSRB 2.3 : Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. in depth, compacting each deposited layer by ramming after watering with lead upto SO m. and lift upto 1.S m. including cost of all labour complete as per specifications. specification. No. KBS with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	56.16	227.91	23.39	5330.07	23.39	5330.07
38	KSRB 5-11 : Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not lessthan 1800 kg/m3 and having a minimum average compressive strength 5.00 N/mm2 confirming to IS 2185 (Part) : 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charegs, scaffolding, curing complete as per specifications. KBS No.5.4 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	317.91	1034.11	314.63	325364.98	314.63	325364.98

Scanned by TapScanner

39	KSRB15-3.10 : Providing 20mm thick cement plaster in single coat with cement mortar 1:3, to stone masonry & concrete surface including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	336.95	327.69	329.47	107965.60	329.47	107965.60	
40	KSRB 15.3.1 Providing 12mm thick cement plaster in single coat with cement mortar 1:3, to brick masonry including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	216.33	239.25	216.33	51757.21	216.33	51757.21	
41	KSRB15-3-13 : Providing 12mm thick cement plaster in single coat with cement mortar 1:3, to ceiling including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	59.80	266.46	59.80	15934.58	59.80	15934.58	
42	KSRB 15.10.2 Providing white washing for every one additional coat with lime of approved quality, to give an even shade including cost of materials, labour, complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	216.33	6.80	216.33	1471.44	216.33	1471.44	
43	KSRB 15.10.4 Providing white washing to ceiling and / or sloping roof surface with additional one coat with lime of approved quality, to give an even shade including cost of materials, labour, complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	59.80	7.94	59.80	474.65	59.80	474.65	

Scanned by TapScanner

Scanned by TapScanner

48	KSRB 14.14-5: Providing Ceramic tiles of approved make,shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick, cement mortar 1:3 mix, flush pointing with white cement using colour pigment , including cost of materials, labour, curing, complete as per specifications. - for Ceramic Tiles 400 x 400mm on a bed of 20mm thick with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	40.20	1438.91	40.20	57844.14	40.20	57844.14
49	KSRB 14-17.2 : Providing skirting, dado, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over rough plaster surface (excluding cost of rough plastered surface which should be measured and paid separately) using glazed tiles of approved make and size including cost of materials, labour, complete as per specifications. Specification No.KBS 14.16, 14.17 - Colour glazed tiles 30x60 cms 6mm thick with border of size 30 x 10 cms with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	128.73	1850.51	128.73	238216.38	128.73	238216.38
50	KSRB 9.4-3 : Providing Mathi / Nandi wood frames of doors, windows, clerestory windows, ventilators and other frames, wrought, framed or assembled including making plaster groves (excluding cost of cement concrete and side clamps), but including cost of materials, labour, HOM of machineries complete as per specifications. Specification No. KBS 9.33 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Cum	0.67	1850.51	0.64	1178.78	0.64	1178.78
51	KSRB 9.5-3 : Providing and fixing in position fully panelled Mathi/Nandi wood shutters for doors, styles and rails of 40mm. thick with bottom and lock rails 180mm wide top rail and styles 100mm wide as per drawing and panels of 25mm thick including cost of materials, labour, HOM of machineries complete as per specifications. (excluding cost of fixtures) Specification No. KBS 9.34 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	7.56	4313.33	7.38	31832.34	7.38	31832.34

Scanned by TapScanner

52	Providing and fixing factory made single leaft rigid GRP Sandwich composite door shutter of 32mm thick, laminated with two GRP skins with wood grain finish, fabricated using U.V-stabilized Isopthalic Gelcoat and on layer of 45 gsm E-Glass Chopped strand Mat (CSM), impregnated with orthopthalic polyster resin. The thickness of the skins shall not be less than 1.5mm. Expanded Polystyrene (EPS) structural foam panel of 29mm thickness and a density of 20 Kg/m3 shall be used as core material. Wooden reinforcements made of Seasoned Salwood block of cross section not less than 28mmx32mm and also necessary salwood reinforcements for fixing the metal fittings such as tower bolts, aldrops, handles, etc, shall be provided. A structural adhesive compatible with EPS foam shall be used for bonding the core material, the Salwood reinforcement and the skins. The material and process for manufacturing the door shutters shall confirm to RV/TIFAC Composites Design centre Standards and specifications and the door shutters tested in confiramation to IS 4020-1994. The finish of shutter will be plain colour White/Ivory/Beige/Light Grey or any other colour using high quality pigments. Exclusing cost of fixtures and inclusive of supply of shutters to respective work spot. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	**17.01**	3401.68	17.01	57862.51	17.01	57862.51	

Scanned by TapScanner

53	KSRB 7.10 : Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using double track window frame section of size 61.85x31.75mm. with 1.2mm thick, bottom section weight 0.695 kg/m, sides and top sections 1.3 mm. thick weight 0.659 kg/m; and shutter comprising top and bottom section of size 40mmx18mm, 1.25mm thick 0.417 kg./m; shutter outer side 40mmx18mm, 1.25mm.thick weight 0.417 kg/m, shutter interlock section 40mmx26.7mm, 1.1mm thick, weight 0.469 kg/m. the shutters mounted on nylon rollers with approved quality of fixtures such as aluminium handles tower bolts etc.; and providing and fixing 5.5mm. thick plain glass for shutters fitted with rubber beading aluminium sections including cutting to required length, joints mitred subdividing the frame tenonned and rivetted in the assembled frame stiffened with end clips at corners angles etc., and fixed to the walls, lintels, floor beams/cills as the case may be with necessary steel screws, raul plugs, or teak wood gatties including cutting masonry or concrete and making good the original surface using cement mortar, aluminium sections pretreated for removal of any Specification No. KBS using aluminium section anodized to 12 - 15 microns. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	5.76	4794.10	5.76	27613.99	5.76	27613.99
54	KSRB 15-17.4 : Applying priming coat over new wood surface and / or wood based surface, after brushing with ready mix enamel priming paint including preparing the surface after thoroughly cleaning oil, grease, dirt and foreign matter, sand papering and knotting ready mix paint including cost of materials, labour, complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	7.56	56.69	7.38	418.41	7.38	418.41
55	Providing and applying painting two coats (excluding priming coat) on new wood surface and / or wood based surface with enamel paint to give an even shade, cleaning the surface of all dirt, dust and foreign matter, sand papering including cost of materials, labour, complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	Sqm	7.56	109.99	7.56	831.51	7.56	831.51

Scanned by TapScanner

56	KSRB 13-11.1 : Providing and placing on terrace, polyethylene water storage tanks as per IS 12701 : 1996 with manhole lid and suitable locI<ing arrangements, making holes of suitable diameter for inlet, outlet and over flow pipes, including cost of all materials, labour, transport charges, HOM of equipments and testing complete as per specifications.(For 1 000 litre capacity) Specification No.KBS 13.22 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	4.00	7742.21	4.00	30968.86	4.00	30968.86	
57	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC solvent cement & the cost of cutting chases & making good the same including testing of joints complete. (Concealed work including cutting chases and good the walls etc.) - 20mm nominal OD pipes. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	m	200.00	266.46	200.00	53292.92	200.00	53292.92	
58	Providing and fixing Chorinated Poly Venyl Chloride (CPVC) pipes conforming to IS 15778, having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings including fixing the pipe with clamp at 1.00 mtr spacing. This includes jointing of pipes and fittings with one step CPVC solvent cement & the cost of cutting chases & making good the same including testing of joints complete. (Concealed work including cutting chases and good the walls etc.) - 25mm nominal OD pipe with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	m	200.00	332.23	200.00	66446.07	200.00	66446.07	
59	KSRB13-8.5 : Providing and fixing to wall, ceiling and floor, low density polyethylene pipes 6.00 kgf/sq.cm working pressure 110mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor, including cost of all materials, labour charges, HOM of equipments and testing complete as per specifications. Specification No.KBS 13.2.15.1 / 13.9 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	m	100.00	430.88	100.00	43087.90	100.00	43087.90	

Scanned by TapScanner

60	KSRB 11-15.3 : Providing and fixing 453x357mm dia rectangular shape mirror with plastic moulded frame of approved make and shade with 6mm thick hard board backing including cost of materials, labour complete as per specifications. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	unit	5.00	1288.10	5.00	6440.50	5.00	6440.50
61	Providing and fixing 7.5 cms to 15.00 cms dia NP grating 100 mm dia. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	10.00	170.08	10.00	1700.84	10.00	1700.84
62	Providing and fixing CI Nahani trap of approved make conforming to ISI specifications and construction of Cistern in M-15 as per directions (Rate is inclusive of cost of materials and fixtures and conveyance of materials to work spot). - 10cms x 7.5cms with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	23.00	283.47	23.00	6519.88	23.00	6519.88
63	KSRB13-6.1-1 : Providing and fixing in position brass bib cock of approved quality 15mm nominal bore including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification No.KBS 13.2.2 / 13.3 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	23.00	215.44	23.00	4955.11	23.00	4955.11
64	KSRB13-6.3-3 : Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) 25mm nominal bore including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification No.KBS 13.2.6 / 13.3. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	8.00	509.12	8.00	4072.94	8.00	4072.94
65	KSRB13-6.3-3 : Providing and fixing in position brass gate valve with C.I wheel of approved quality (screwed end) 20mm nominal bore including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification No.KBS 13.2.6 / 13.3. with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	each	12.00	380.99	12.00	4571.85	12.00	4571.85

Scanned by TapScanner

66	Constructing brick masonry inspection chamber 450x450mm, and 450mm depth, (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover withframe (light duty) 455x610mm internal dimensions, total weight of cover with frame to be not less than 38 kg (weight of cover 23kg and weight of frame 15 kg) R.C.C. top slab with cement concrete M 15 with 20mm and downsize granite metal, foundation concrete M 5 with 40mm and downsize granite metal inside plastering 12mm thick with cement mortar 1:3, finish smooth with a floating coat of cement on walls and bed concrete complete as per standard design including cost of materials, labour charges, curing complete as per specifications. Specification No. KBS 450x450mm and 450mm depth (clear inside dimension) for single pipeline, using table moulded non-modular bricks of class designation 50 in cement mortar 1:5, C.I cover withframe (light duty) 450x450mm with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	No	12.00	6009.63	12.00	72115.53	12.00	72115.53	
67	KSRB 11 -6 : Providing and fixing white vitreous china clay, water closet European type (Pedestal type, S-trap) with black solid plastic seat and lid, C.P brass hinges, rubber buffers. 10 litre white glazed I vitreous china clay low level, flushing cistern (all are approved make) with fittings, C.1 I M.S brackets, 40mm diameter flush bend with fittings and clamps, overflow arrangements with specials and 25mm mosquito proof coupling of approved design, painting of fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications.	Each	10.00	5450.62	10.00	54506.19	10.00	54506.19	
68	KSRB 11-11.1 : Providing and fixing white vitreous china clay, flat back wash basin size 630x450mm with a pair of 15mm C.P brass pillar taps with C.I / M.S brackets, 32 mm C.P. brass waste of standard pattern, painting of fittings and brackets, cutting and making good the wall and floor wherever required, including cost of materials, labour complete as per specifications. Specification No. KBS 11 with all lead and lift , loading and unloading and allother incidental charges etc., complete as per specification and direction of the engineer-in-charge of the work	unit	8.00	4543.51	8.00	36348.04	8.00	36348.04	

Scanned by TapScanner
